



7739 Edgar Industrial Way
Red Deer, Alberta
Canada T4P 3R2
Tel: 1-403-346-4487
Fax: 1-403-347-3312

Test Certificate

Serial Number: 1310-597
Date: October 24, 2013
Customer: Huracan Pty Ltd
Purchase Order: JON
Sales Order: 38580
Description of Material: Aluminum 20k Line Clamp
Working Load Limit: 20000 lbs
Description of Test: Horizontal Pull Test
Proof Load: 25000 lbs
Test Machine: Hydraulic tension puller
Date Calibrated: March 19, 2013
Remarks: Passed Test


We hereby certify that the above described material will comply with the specifications listed above.

Test Conducted By:

Name: Derek Forrester

Signature: 

**Huracan Pty Ltd
20K Wireline Clamp
S/N: 1310-597**

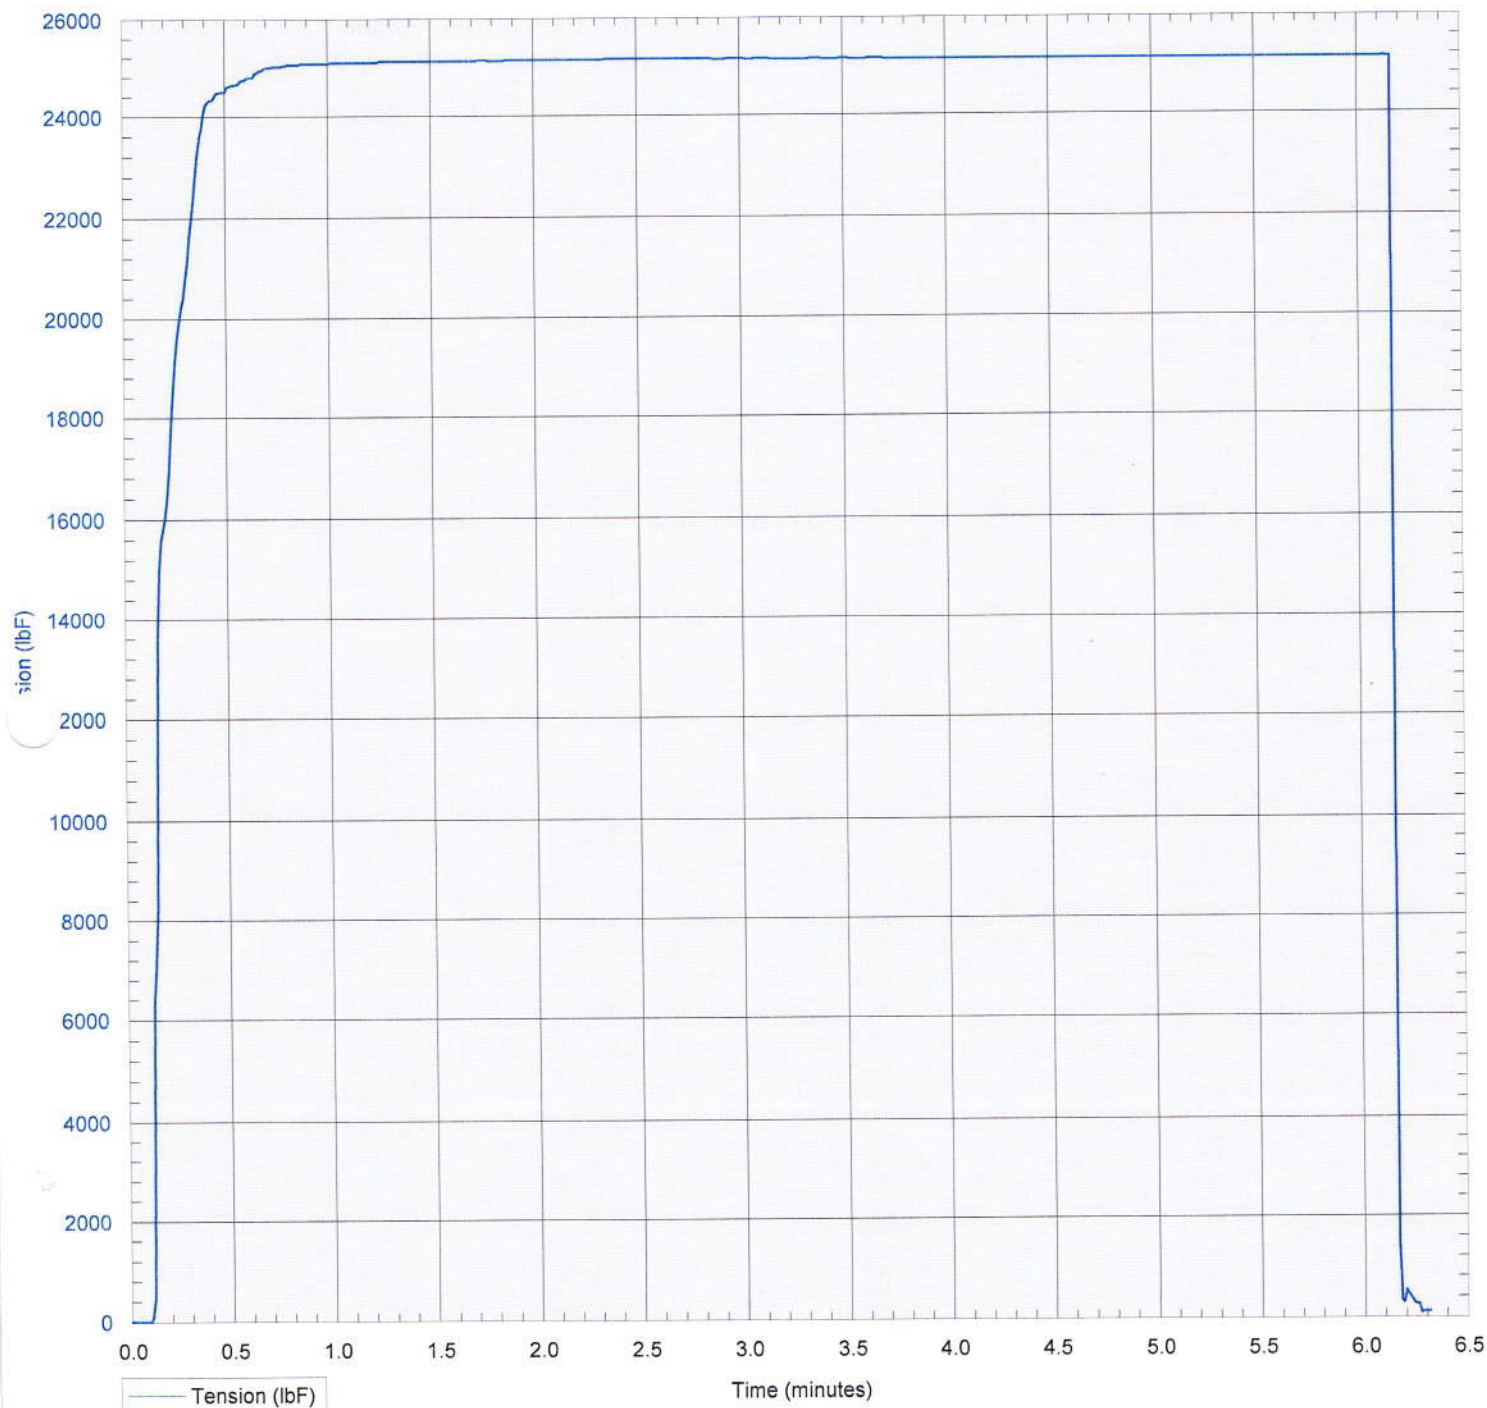

Test Conducted On: October 18, 2013 11:08:48 AM
Transducer Data: LP-131-150K s/n LP1206
Calibrated On: March 19, 2013
Test Conducted By: Jacqueline Avery
Witnessed By: Derek Forrester
Work Order: 38580
Proof Test Load = 25000 lbs
Work Load Limit = 20000 lbs



www.integricert.com

Toll Free: 1-866-285-1306

Integricert, LLC

Load Testing, Inspection and Rigging

HOUMA LOCATION:
206 S. LaCarpe Cir.
Houma, LA 70360

Ph: (985) 868-6355
Fax: (985) 868-6356

MAIN LOCATION:
608 Hangar Drive
New Iberia, LA 70560

Ph: 337-365-1022
Fax: 337-365-1024

HOUSTON LOCATION:
6529 Cunningham Rd. #2303
Houston, TX 77041

Ph: (832) 243-5838
Fax: (832) 243-5840



CERTIFICATE OF Load Test

Customer	PO Number	Job Number	Equipment Number	Certificate Number
MIDSOUTH RENTAL & COMPLETION SE	PO-14-0324WS		SWH-D-1403-01	N-74167-1-1

ITEM
TESTED

LOAD TEST - HALF MOON SHEAVE WHEEL.
S/N: SWH-D-1403-01
SWL = 3,000 LBS
P/L = 3,000 LBS

Load Test	Tested By	Test Date	Expires (Months)	Re-Test Date
	Jeremiah Pryor	03/25/14	60	03/25/19

Tare Weight

SWL/Payload

3,000 LBS

Max Gross Weight

Proof Load Applied

3,000 LBS

Load Test Procedure Used

LT-AHP-001 REV B

NDT Ticket Number

Load Testing Unit

450K LOW RANGE CHANT TEST BED, CALIBRATED ON: 10/01/13,
BEARING S/N: 236857

Field Ticket

N-74167

In subjecting this product to the test/tests described, Integricert does not warrant the product in any manner, or certify its fitness or suitability for any specific use. To the extent this certificate represents a proof load test of equipment, the product described has been subjected to, and passed, a proof load test of the top and bottom side and end rails, corner posts, padeyes, and all welds joining same, as applicable; refer to the NDT ticket number for particulars concerning this test.

WARNING!!! Use of this product is beyond the control of IntegriCert, LLC. The purchaser and/or end user is solely responsible for the usability and suitability of this product. Always check the rated capacity to assure that the product meets the requirements of its intended application/use. The end user must inspect this product for defects or damage prior to each use and should immediately remove from service any defective or questionable product.

R-536 Rev B

Signature:

Nick Orlando

Date: 03/25/14

Stress Testing, Inc. Inspection Division

(337) 288-8082

1037 Jolie Blonde Road Breaux Bridge, Louisiana 70517

davstresstesting@aol.com

Certificate of Compliance

Customer: ArkLatex

Date: 06 MAR 13

Serial Number: # ALK001

Description: BOX SWIVEL

Certification 13-02-830

NDE- Liquid Dye Penetrant Inspection

TYPE OF INSPECTION LP/VISUAL X

Penetrant: Batch Type: Spot Check SKL WP-2

Batch #09K01K

Developer: Batch Type: Spot Check SKD-S2

Batch #08M22K

Accepted: X

Rejected:

Comments: 1 Padeye and all load bearing areas inspected to STI PROCEDURES (ASTM E-165-2003 , ASTM E 1209, ASTM E 1220, API RP 5A5). **ALL OK**

Inspector: RODNEY WRIGHT (001)

Level II MT, PT, VT

STRESS TESTING, INC.

1037 Jolie Blonde Rd.

Breaux Bridge, La. 70517

(337) 288-8082

Certification of Hydraulic Proof Load Test

Test Performed By: Dave Tumlin

Job Number: 13-03-620T

Certification Issued To: Arklatex

Unit No.	Description	Certification No.	Test Date	Tare / WLL (lbs)	Load Applied (lbs)	MGW (lbs)
#ALK-001	6"x1"x3" Box Swivel Load Test as Per BHP Specifications	13-03-620T	03-06-13	Tare: 5 lbs WLL: 495 lbs	1,000 Lbs	500 lbs

Noticeable Deformities upon Visual Inspection: Yes ☐ No ☒ Slings Visually Inspected: Yes ☐ No ☒

Unit Approved for Service: Yes ☒ No ☐ Stress Testing, Inc.

Original Certification: Yes ☒ No ☐ Date: 03-06-2013

By signing this certificate neither the inspector nor his employer makes any warranty expressed or implied, concerning the equipment described in this report. Furthermore, neither the inspector nor his employer shall be liable in any manner for any personal injury or property damage or loss of any kind arising from or connected with this inspection. As the use of this product is beyond the control of Stress Testing, Incorporated, the owner and/or user is solely responsible for the usage of this product.
